Integration Programme - High Level Milestones
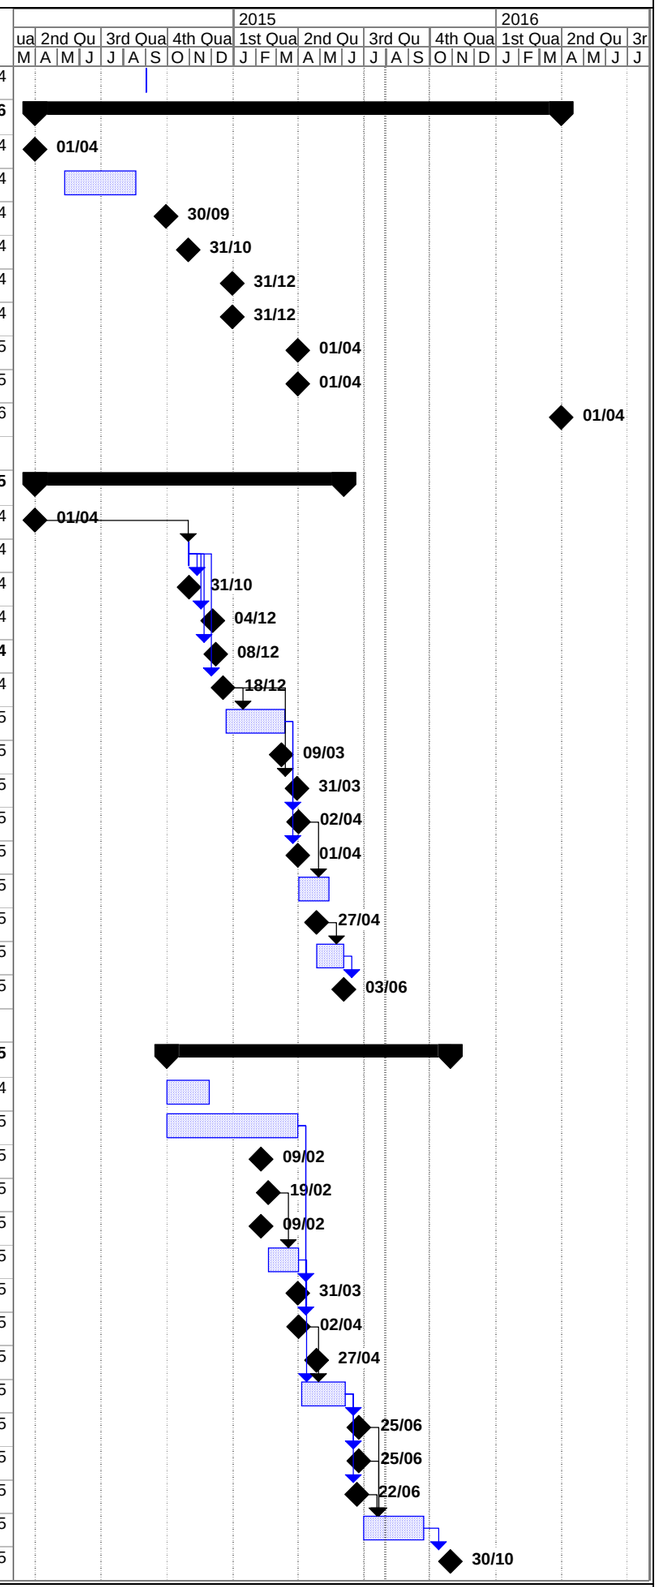
ID	Task Name	Duration	Start	Finish
1		1 day?	Tue 02/09/14	Tue 02/09/14
2	**National Timelines - 2014 - 2016**	**523 days?**	**Tue 01/04/14**	**Fri 01/04/16**
3	Act Receives Royal Assent	0 days	Tue 01/04/14	Tue 01/04/14
4	Consultation (Draft Regs)	71 days?	Mon 12/05/14	Mon 18/08/14
5	Response to Consultation Published	0 days	Tue 30/09/14	Tue 30/09/14
6	Orders and Regs Laid in Parliament	0 days	Fri 31/10/14	Fri 31/10/14
7	Orders and Regs come into force	0 days	Wed 31/12/14	Wed 31/12/14
8	Guidance Completed and Published	0 days	Wed 31/12/14	Wed 31/12/14
9	Integration Schemes Must be Submitted to Scottish Govt	0 days	Wed 01/04/15	Wed 01/04/15
10	Community Health Partnerships Cease	0 days	Wed 01/04/15	Wed 01/04/15
11	Integration Arrangements Need to be in Place	0 days	Fri 01/04/16	Fri 01/04/16
12				
13	**Scheme of Integration**	**307 days?**	**Tue 01/04/14**	**Wed 03/06/15**
14	Outline Scheme of Integration Produced	0 days	Tue 01/04/14	Tue 01/04/14
15	Outline Scheme issued to Work Stream Groups for Population	1 day?	Fri 31/10/14	Fri 31/10/14
16	Produce 1st Draft of the Scheme of Integration	0 days	Fri 31/10/14	Fri 31/10/14
17	Presentation of Draft Scheme of Integration to NHS Board	0 days	Thu 04/12/14	Thu 04/12/14
18	**Presentation of Draft Scheme of Integration to the Shadow Board**	**0 days**	**Mon 08/12/14**	**Mon 08/12/14**
19	Presentation of Draft Scheme of Integration to Council	0 days	Thu 18/12/14	Thu 18/12/14
20	Formal Consultation on the Scheme of Integration	60 days?	Mon 22/12/14	Fri 13/03/15
21	**Update Draft Scheme of Integration presented to Shadow Board as Work in Progress (next meeting of IJB is 27/4/15)**	0 days	Mon 09/03/15	Mon 09/03/15
22	Final Integration Scheme presented to NHS Board	0 days	Tue 31/03/15	Tue 31/03/15
23	Final Integration Scheme presented to Council	0 days	Thu 02/04/15	Thu 02/04/15
24	Final Integration Scheme Submitted to Scottish Govt	0 days	Wed 01/04/15	Wed 01/04/15
25	Review by Scottish Govt	30 days	Thu 02/04/15	Wed 13/05/15
26	**Final Integration Scheme to be presented to the Integration Joint Board**	0 days	Mon 27/04/15	Mon 27/04/15
27	Submission lies in Parliament	28 days	Mon 27/04/15	Wed 03/06/15
28	Order Issued	0 days	Wed 03/06/15	Wed 03/06/15
29				
30	**Strategic Commissioning Plan**	**282 days?**	**Wed 01/10/14**	**Fri 30/10/15**
31	Pre-drafting Engagement with Practitioners and Identified Stakeholders	43 days?	Wed 01/10/14	Fri 28/11/14
32	Drafting of Strategic Commissioning Plan	130 days?	Wed 01/10/14	Tue 31/03/15
33	Proposals for Establishing Strategic Planning Group to the NHS Board (Date to be confirmed)	0 days	Mon 09/02/15	Mon 09/02/15
34	Proposals for Establishing Strategic Planning Group to Council	0 days	Thu 19/02/15	Thu 19/02/15
35	**Proposals for Establishing Strategic Planning Group to the Shadow Board**	0 days	Mon 09/02/15	Mon 09/02/15
36	Recruitment/Establishment of the Strategic Planning Group	30 days	Thu 19/02/15	Wed 01/04/15
37	1st Draft of the Strategic Commissioning Plan - for Consultation - to the NHS Board for agreement (Date to be confirmed)	0 days	Tue 31/03/15	Tue 31/03/15
38	1st Draft of the Strategic Commissioning Plan - for Consultation - to Council for agreement	0 days	Thu 02/04/15	Thu 02/04/15
39	**First Draft of the Strategic Commissioning Plan completed and presented to the Integration Joint Board**	0 days	Mon 27/04/15	Mon 27/04/15
40	Second Draft of the Strategic Commissioning Plan developed in engagement with stakeholders	45 days	Mon 06/04/15	Fri 05/06/15
41	2nd Draft of the Strategic Commissioning Plan - for Consultation - to the NHS Board for agreement	0 days	Thu 25/06/15	Thu 25/06/15
42	2nd Draft of the Strategic Commissioning Plan - for Consultation - to Council for agreement	0 days	Thu 25/06/15	Thu 25/06/15
43	**Second Draft of the Strategic Commissioning Plan completed and presented to the Integration Joint Board**	0 days	Mon 22/06/15	Mon 22/06/15
44	Formal Consultation on the Strategic Commissioning Plan	60 days	Wed 01/07/15	Tue 22/09/15
45	**Strategic Commissioning Plan Agreed by the Parent Bodies and Integration Joint Board**	0 days	Fri 30/10/15	Fri 30/10/15
